



**HUOT SRY TRADE & CONSTRUCTION CO., LTD.**

# Monthly Report Jun -2024

**TRANSMISSION LINE  
GS12 TO STUNG TATAY**

**PREPARED BY : SEN RINET  
SITE SURVEYOR**

Address: 45, St P06, Sangkat Phnom Penh Thmey, Khan Sensok, PhnomPenh, Cambodia  
Contact number: (+855)81 700 927, Email Address: huotsry@gmail.com

# PROJECT PROGRESS REPORT

**PROJECT: PCL07**

---

## **1. SUMMARY OF CONSTRUCTION PROGRESS AS OF JUN 2024 GS12 TO STUNG TATAY TRANSMISSION LINE.**

---

<b>PROJECT PROGRESS</b>
1. Pad and Chimney Foundation
2. Tower Erection
3. Tree Cutting
4. Stringing
<b>OVERALL PROJECT</b>

---

## **LIST OF MANPOWER**

---

<b>DESCRIPTION</b>
1. Project Manager
2. Site Manager
3. Site Supervisor
4. Site Engineer
5. Safety Officer
6. Site Procurement
7. Stock Keeper
8. Foreman
9. Surveyor
10. Concrete Team
11. Rebar Team
12. M&E Team
13. Erection Team
14. Security

---

---

## LIST OF MACHINERY

---

DESCRIPTION
1. Concrete Vibrating
2. Steel Cutting Machine
3. Steel Bending Machine
4. Dump Truck
5. Welding Machine
6. Container Office and Stock
7. Generator
8. Mobile Concrete Mixing Machine
9. Concrete Mixing Truck
10. Excavator
11. Mobile Crane
12. Trailer
13. Breaker
14. Cambodia Car

---

# 1. Access Road Works



Access Road Work



Access Road Work



Access Road Work



Access Road Work (Breaking stone)



Repair access Road Work



Access Road Work( Drainage pile)

# 1. Access Road Works



Access Road Work



Access Road Work



Access Road Work



Access Road Work (Breaking stone)



Access Road Work (Breaking stone)



Access Road Work

# 1. Sending Materials Works



Sending materials.



Sending materials.



Access Road Work



Sending materials.



Sending materials.



Sending materials.

# 1. Soil Excavation Works (T-C080-1)



Soil excavation



Breaking stone



Soil excavation



Breaking stone



Breaking stone



Soil excavation

# 1. Lean Concrete Works (T-C080-1)



Casting concrete lean



Casting concrete lean



Casting concrete lean



Casting concrete lean



Casting concrete lean



Casting concrete lean

# 1. Stub Setting Works (T-C080-1)



Stub setting



Stub setting



Stub setting



Stub setting



Stub setting



Stub setting

# 1. Base Foundation Works (T-C080-1)



Rebar installation



Rebar installation.



Formwork installation.



Rebar installation.



Rebar installation & formworks.



Cleaning.

# 1. Base Foundation Works (T-C080-1)



Casting concrete base .



Casting concrete base finish.



Casting concrete base .



Casting concrete base finish.



Casting concrete base .



Casting concrete base finish.

# 1. Chimney Foundation Works (T-C080-1)



Casting concrete chimney .



Concrete vibration.



Casting concrete chimney .



Concrete vibration.



Casting concrete chimney .



Casting concrete chimney .

# 1. Soil Excavation Works (T-C085)



Soil excavation



Soil excavation



Soil excavation



Soil excavation



Soil excavation



Soil excavation

# 1. Lean Concrete Works (T-C085)



Concrete mixing



Concrete mixing



Casting concrete lean



Casting concrete lean



Casting concrete lean



Casting concrete lean

# 1. Stub Setting Works (T-C085)



Set stub.



Set stub.



Set stub.



Set stub.



Set stub.



Set stub.

# 1. Base Foundation Works (T-C085)



Arrengement rebar of the base .



Install rebar of the column.




Install formworks of the base .



Install rebar and formworks



Install rebar.

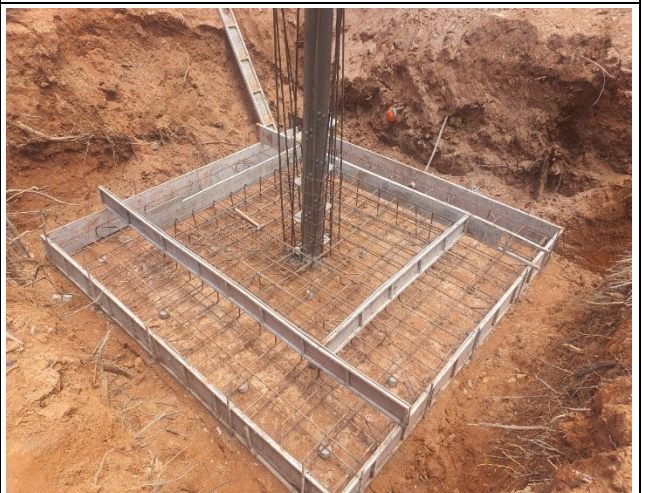

Install rebar and formworks.

# 1. Base Foundation Works (T-C085)



Concrete mixing for the base .




Casting concrete base



Concrete vibration base.



Concrete vibration base.

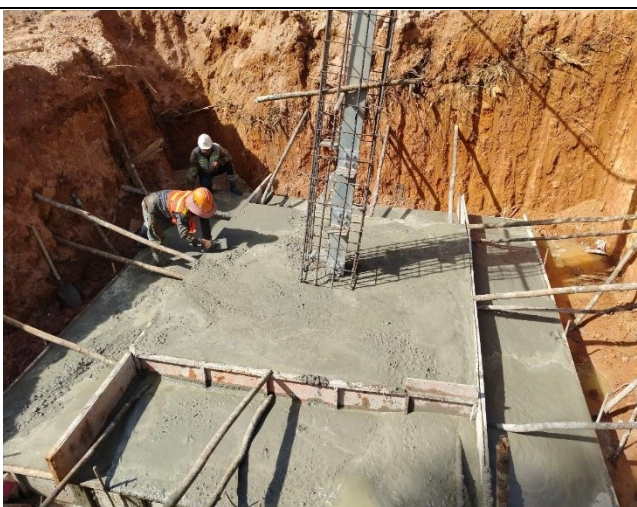

Concrete leveling .



Concrete finish.

# 1. Chimney Foundation Works (T-C085)



Covering concrete.



Covering concrete.



Covering concrete.



Concrete vibration base.



Concrete mixing



Preparation casting concrete

# 1. Chimney Foundation Works (T-C085)



Casting concrete of the chimney.



Concrete vibration.



Concrete vibration.



Casting concrete of the chimney.



Casting concrete of the chimney.



Concrete finish.

# 1. Soil Excavation Works (T-C113)



Measuring for excavatoin of the pit.



Soil excavatoin of the pit.



Soil excavatoin of the pit.



Soil excavatoin of the pit.



# 1. Soil Excavation Works (T-C113)



Casting concrete lean



Casting concrete lean



Casting concrete lean



Casting concrete lean



Casting concrete base.



Casting concrete lean

# 1. Stub setting Works (T-C113)



Stub setting



Stub setting



Stub setting



Stub setting



Stub setting



Stub setting

# 1. Base Foundation Works (T-C113)



Installation rebar



Installation rebar



Casting concrete



Concrete vibration



Casting concrete



Casting leveling.

# 1. Chimney Foundation Works (T-C113)



Concrete mixing for the chimney



Casting concrete chimney



Casting concrete



Concrete vibration



Casting concrete



Check of the stub

# 1. Soil Excavation Works (T-C112)



Breaking stone



Soil excavation



Soil excavation



Soil excavation



Casting concrete



Casting leveling.

# 1. Lean Concrete Works (T-C112)



Casting concrete lean



Casting concrete lean



Casting concrete lean



Casting concrete lean



Casting concrete lean



Casting concrete lean

# 1. Stub Setting Works (T-C112)



Stub setting



Stub setting



Stub setting



Stub setting



Stub setting



Stub setting

# 1. Base Foundation Works (T-C112)



Installation rebar base .



Installation formwork base.



Installation rebar& formwork base.



Installation rebar base .



Installation rebar& formwork base.



Installation rebar& formwork base.

# 1. Base Foundation Works (T-C112)



Casting concrete base .



Casting concrete finish.



Concrete mixing .



Casting concrete finish.




Casting concrete



Casting concrete

# 1. Chimney Foundation Works (T-C112)

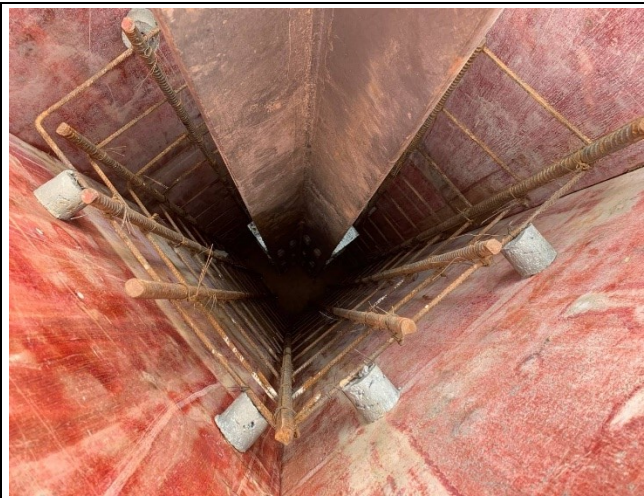

Cover concrete .



Casting concrete chimney.



Casting concrete chimney .



Concrete vibration.

## 2. Tower Erection Works



TA097 Tower erection



TA097 Erection completed.



TA098 Tower erection




TA098 Erection completd.

## 2. Tower Erection Works



TA099 Tower erection

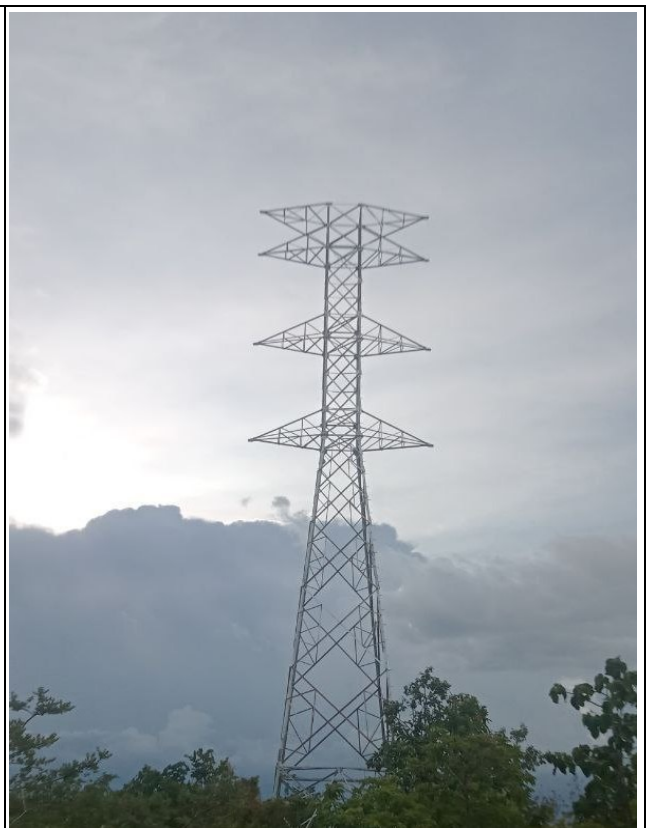

TA099 Erection completed.



TA108 Tower erection



TA108 Erection completd.

## 2. Tower Erection Works



TA118 Tower erection.



TA118 Erection completed.




TA126 Tower erection.



TA126 Erection completd.

## 2. Tower Erection Works

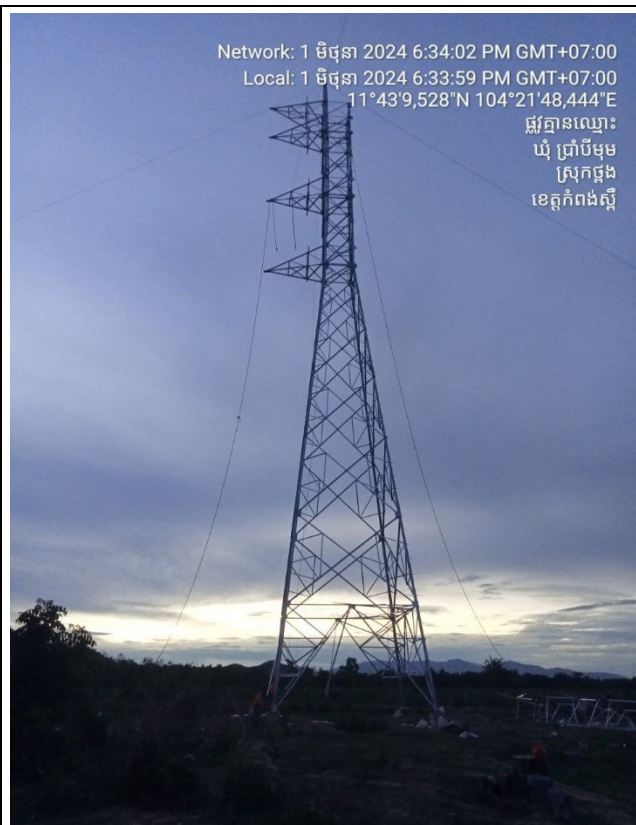

TA124 Tower erection



TA124 Erection completed.



TA125 Tower erection



TA125 Erection completd.

## 2. Tower Erection Works



TA130 Tower erection.



TA130 Erection completed.



TA131 Tower erection.



TA131 Erection completd.

## 2. Tower Erection Works



TA134 Tower erection.



TA134 Erection completed.




TA135 Tower erection.



TA135 Erection completd.

## 2. Tower Erection Works

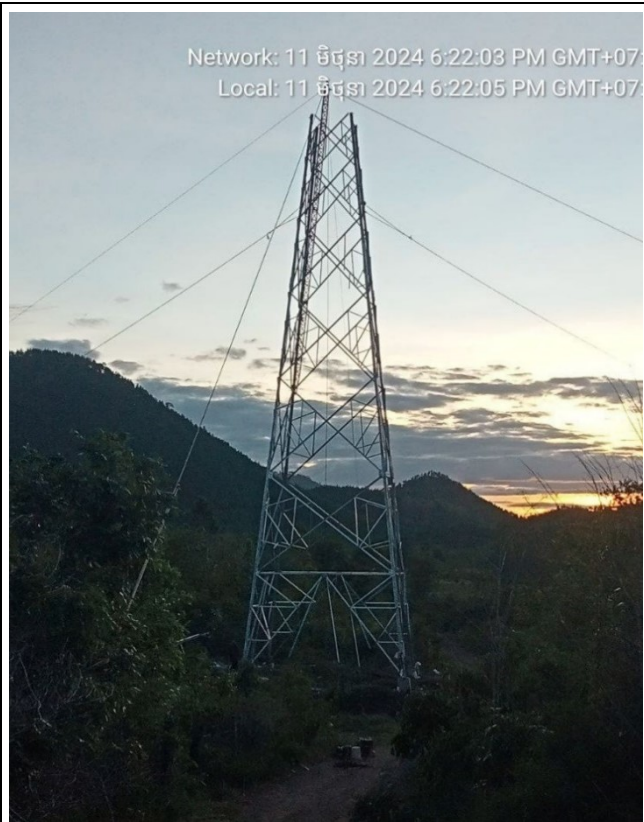

TA138 Tower erection.



TA138 Erection completed.



TA141 Tower erection.



TA141 Erection completd.

## 2. Tower Erection Works



TA151 Tower erection.



TA151 Erection completed.



TA152 Tower erection.




TA152 Erection completd.

## 2. Tower Erection Works



TA156 Tower erection

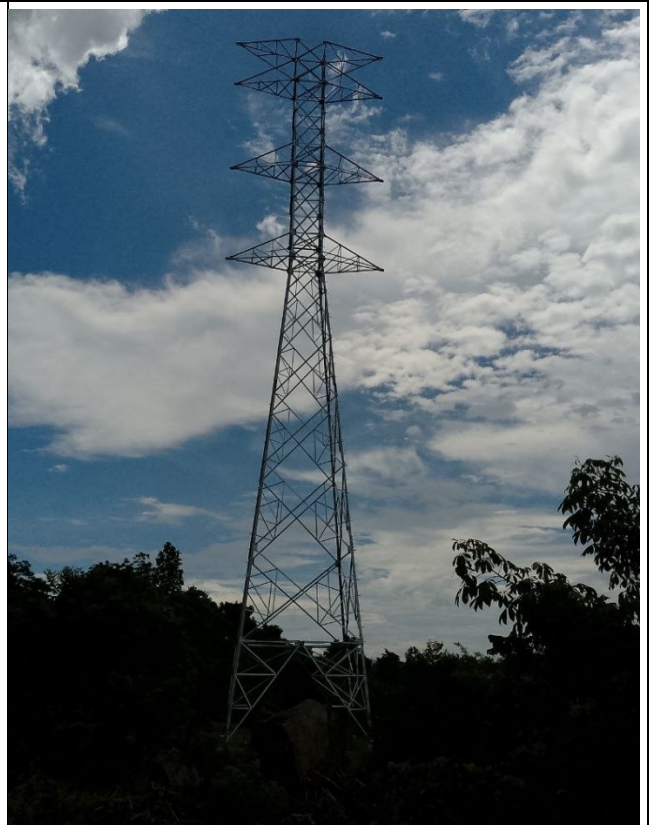

TA156 Erection completed.



TA158 Tower erection



TA158 Erection completd.

## 2. Tower Erection Works



TA168 Tower erection



TA168 Erection completed.



TA180 Tower erection




TA180 Erection completd.

## 2. Tower Erection Works



TA181 Tower erection

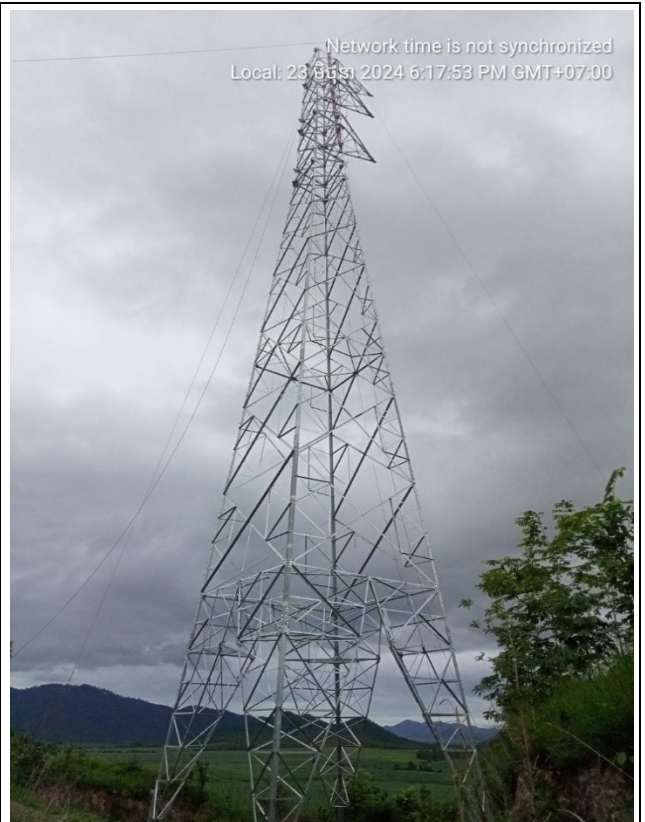

TA181 Erection completed.



TA188 Tower erection



TA188 Erection completd.



### 3. Trees Cutting Works (TC079-TC080)



Trees cutting



Trees cutting



Trees cutting



Trees cutting



Trees cutting



Trees cutting

### 3. Trees Cutting Works (TC084-TC085)



Trees cutting



Trees cutting



Trees cutting



Trees cutting



Trees cutting



Trees cutting

### 3. Trees Cutting Works (TC083-TC084)



Trees cutting



Trees cutting



Trees cutting



Trees cutting




Trees cutting



Trees cutting

#### 4. Stringing Works.

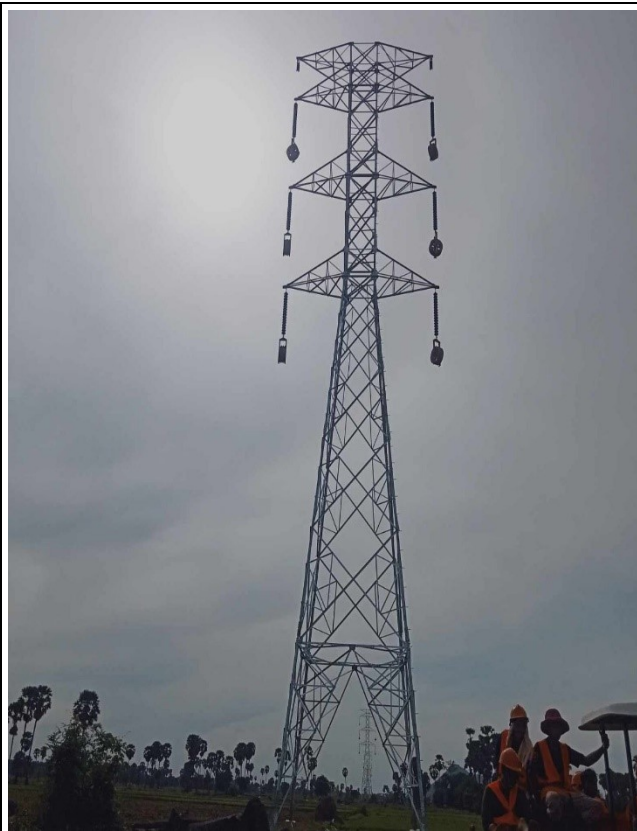

T-A062 Equipp insulator



T-A064 Equipp insulator



T-A065 Equipp insulator



T-A066 Equipp insulator

4. Stringing Works.



T-A068 Equipp insulator



T-A069 Equipp insulator



T-A073 Equipp insulator



T-A074 Equipp insulator

#### 4. Stringing Works.



T-A076 Equipp insulator



T-A077 Equipp insulator



T-A078 Equipp insulator



T-A079 Equipp insulator

#### 4. Stringing Works.



T-A081 Equipp insulator



T-A082 Equipp insulator



T-A087 Equipp insulator



T-A089 Equipp insulator

# 4. Stringing Works.



T-A090 Equipp insulator



T-A091 Equipp insulator



T-A093 Equipp insulator



T-A094 Equipp insulator

**4. Stringing Works.**



T-A095 Equipp insulator



T-A096 Equipp insulator



Installation scaffuding between T-A026, T-A026A



Installation scaffuding between T-A023, T-A024

**Thank you!**
